




Moccasin Wallow Road Improvements from U.S. 41 to U.S. 301 Bi-Weekly Update | April 15, 2024

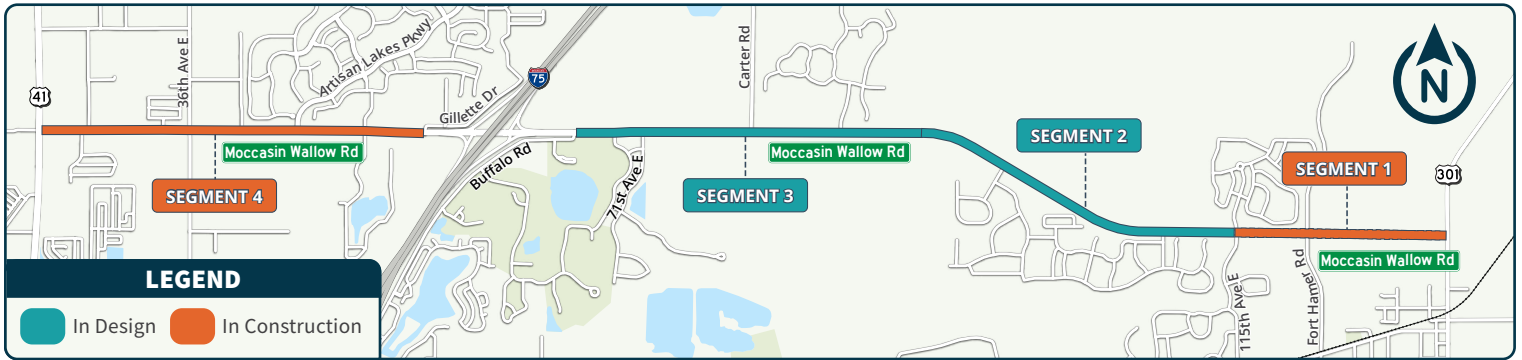

Segment 1 (U.S. Highway 301 to 115th Street East):

ANTICIPATED COST AND CONSTRUCTION SCHEDULE

- Construction Cost:** \$28 Million
- Construction Start:** January 2023
- Completion Date:** Fall 2024

This roadway project will widen approximately 1 mile of Moccasin Wallow Road from 2-lanes to 4-lanes (two in each direction) between U.S. 301 and 115th Street East. This roadway segment will also include a 12-foot wide multi-use path on the north side of Moccasin Wallow Road, a 6-foot wide sidewalk on the south side, and 7-foot wide bicycle lanes in each direction. The four travel lanes will be separated by a 44-foot wide raised median which will accommodate future roadway widening.

Median openings will be provided for access to residential communities and the addition of pedestrian-activated crossings, street lighting, signalized intersections, driveway modifications, and dedicated turning lanes will improve safety and traffic operations throughout the roadway corridor.

This segment also includes construction of a roundabout at the U.S. 301 and Moccasin Wallow Road intersection for more efficient traffic flow and improved safety. Roadway drainage will be improved and stormwater run off will be directed to new linear ponds along Moccasin Wallow Road and county right-of-way near the U.S. 301 roundabout.



Current Activities:

Throughout the month of April 2024, the contractor will continue installing the new storm sewer system, constructing the new roadway, concrete curb, and sidewalk. No lane closures are expected. Motorists are urged to exercise caution and observe the new traffic patterns when traveling in this area.

CONTACT US

- Alice Ramos**
Community Outreach Specialist
- info@MoccasinWallowRoad.com
- (941) 213-1141




Project Website:
www.moccasinwallowroad.com



For more information, scan the QR code to visit the project website.



Moccasin Wallow Road Improvements from U.S. 41 to U.S. 301 Bi-Weekly Update | April 15, 2024

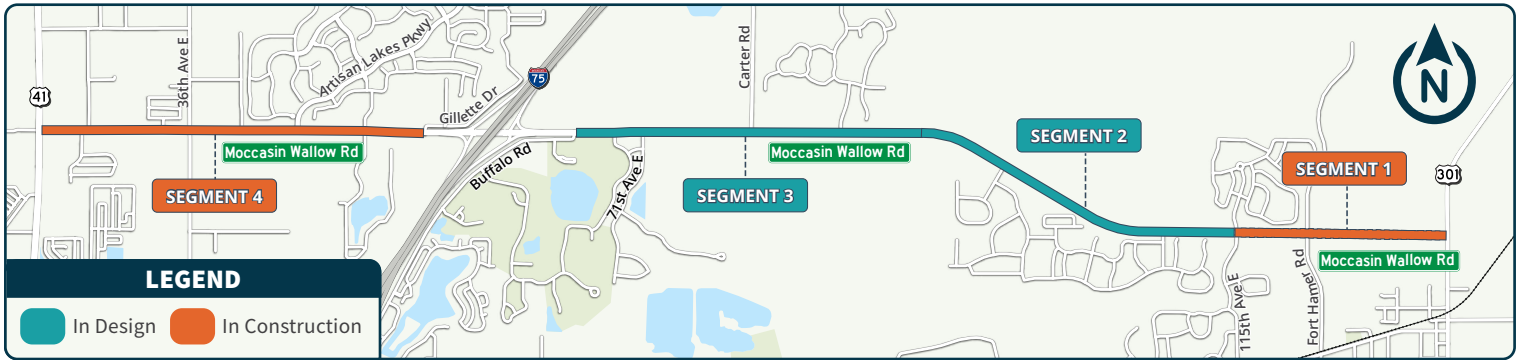

Segment 2 (115th Street East to Bayside Community Church):

ANTICIPATED COST AND CONSTRUCTION SCHEDULE

- Construction Cost:** \$35 Million
- Construction Start:** Fall 2024
- Completion Date:** Mid 2026

This roadway project will widen approximately 1.6 miles of Moccasin Wallow Road from 2-lanes to 4-lanes (two in each direction) between 115th Street East to Bayside Community Church. This roadway segment will also include a 12-foot wide multi-use path on the north side of Moccasin Wallow Road, a 6-foot wide sidewalk on the south side, and 7-foot wide bicycle lanes in each direction. The four travel lanes will be separated by a 44-foot-wide raised median which will accommodate future roadway widening.

Median openings will be provided for access to residential communities and the addition of pedestrian-activated crossings, street lighting, signalized intersections, driveway modifications, and dedicated turning lanes will improve safety and traffic operations. Roadway drainage will be improved and stormwater run-off will be directed to new linear ponds along Moccasin Wallow Road.

Current Activities:

The project is currently advertised for bidding for construction.

Segment 3 (Bayside Community Church to Buffalo Road (east of I-75):

ANTICIPATED COST AND CONSTRUCTION SCHEDULE


- Construction Cost:** \$43 Million
- Construction Start:** Spring 2025
- Completion Date:** Early 2027

This roadway project will widen approximately 1.8 miles of Moccasin Wallow Road from 2-lanes to 4-lanes (two in each direction) between Bayside Community Church to Buffalo Road. This roadway segment will also include a 12-foot wide multi-use path on the north side of Moccasin Wallow Road, a 6-foot wide sidewalk on the south side, and 7-foot wide bicycle lanes in each direction. The four travel lanes will be separated by a 44-foot-wide raised median which will accommodate future roadway widening.

Median openings will be provided for access to residential communities and the addition of pedestrian activated crossings, street lighting, signalized intersections, driveway modifications, and dedicated turning lanes will improve safety and traffic operations. Roadway drainage will be improved and stormwater run-off will be directed to new linear ponds along Moccasin Wallow Road.




Current Activities:

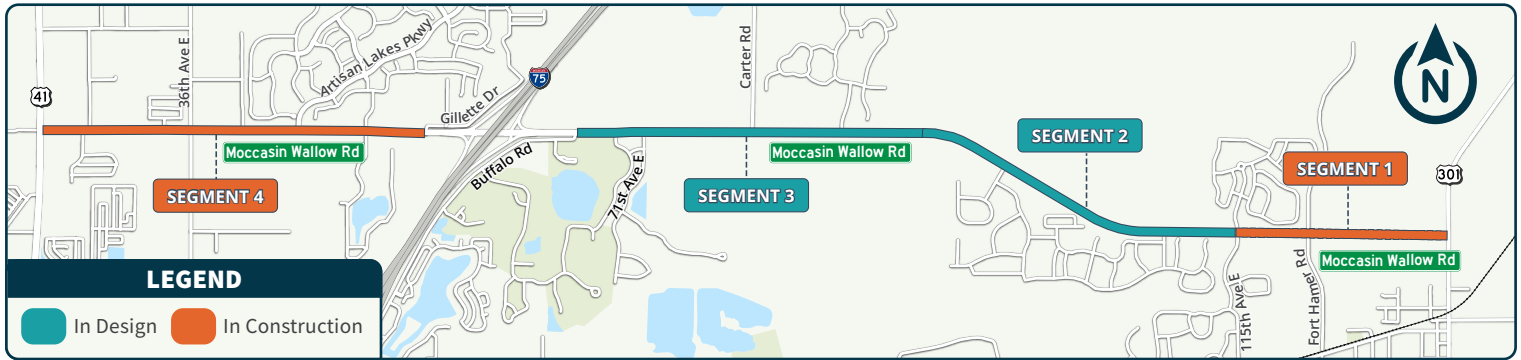This project is currently in design. Land acquisition and environmental permitting are ongoing.



Segment 4 (U.S. 41 to Gillette Drive):

ANTICIPATED COST AND CONSTRUCTION SCHEDULE

-  **Construction Cost:** \$49 Million
-  **Construction Start:** January 2023
-  **Completion Date:** Fall 2024

This roadway project will widen approximately 1.9 miles of Moccasin Wallow Road from 2-lanes to 4-lanes (two in each direction) between Gillette Drive (located just west of I-75) and U.S. 41. This roadway segment will also include a 12-foot wide multi-use path on


the north side of Moccasin Wallow Road, a 6-foot wide sidewalk on the south side, and 7-foot wide bicycle lanes in each direction. The four travel lanes will be separated by a 44-foot-wide raised median which will accommodate future roadway widening.

Median openings will be provided for access to residential communities and the addition of pedestrian-activated crossings, street lighting, signalized intersections, driveway modifications, and dedicated turning lanes will improve safety and traffic operations. Roadway drainage will be improved and stormwater run-off will be directed to new linear ponds along Moccasin Wallow Road.

Current Activities:



Throughout the month of April 2024, the contractor will continue installing the new storm sewer system, light poles and bases, paving, and constructing the new roadway.

As part of the Moccasin Wallow Road Segment 4 Improvements project, traffic on Moccasin Wallow Road will be shifted south to newly constructed roadway from Bud Rhoden Road to Gillette Drive, west of I-75 on Friday, April 26th. Motorists are urged to exercise caution and observe the new traffic patterns when traveling in this area.





Moccasin Wallow Road Improvements from U.S. 41 to U.S. 301 Bi-Weekly Update | April 15, 2024

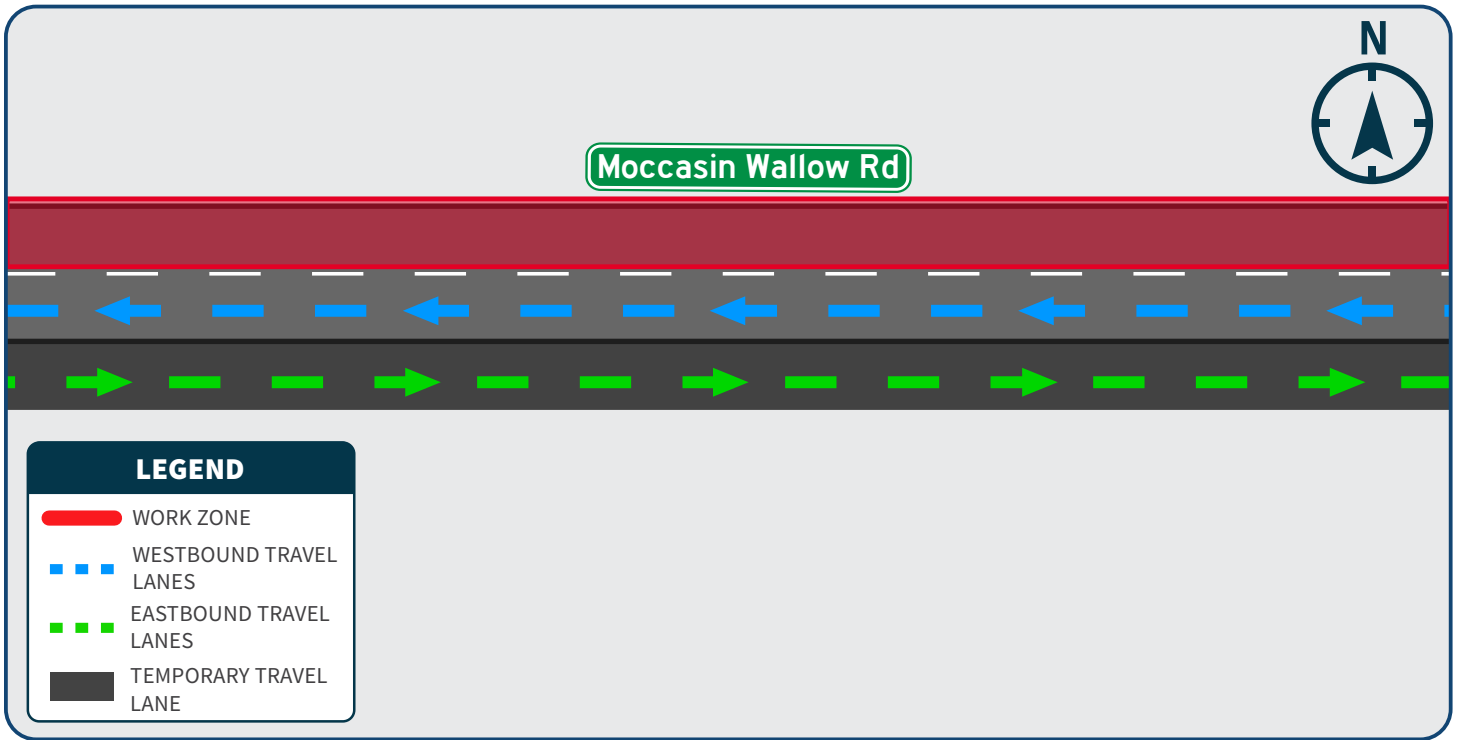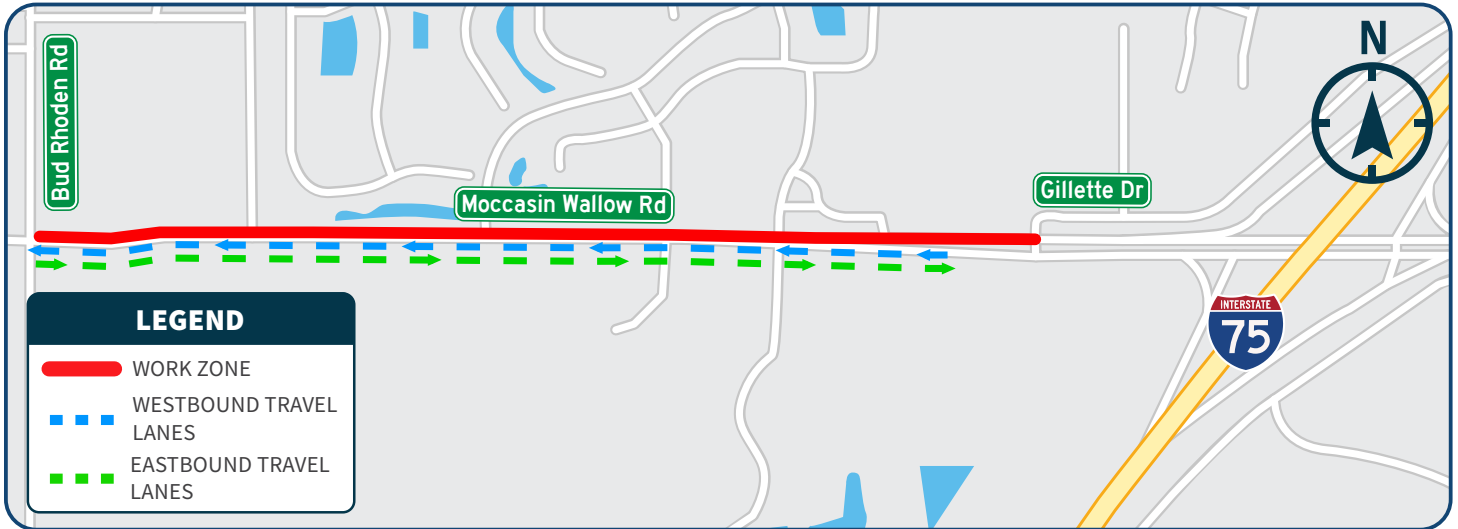

CONTACT US

Alice Ramos
Community Outreach Specialist
 info@MoccasinWallowRoad.com
 (941) 213-1141

Project Website:
www.moccasinwallowroad.com



For more information, scan the QR code to visit the project website.
