




Moccasin Wallow Road Improvements from U.S. 41 to U.S. 301 Bi-Weekly Update | November 20, 2024

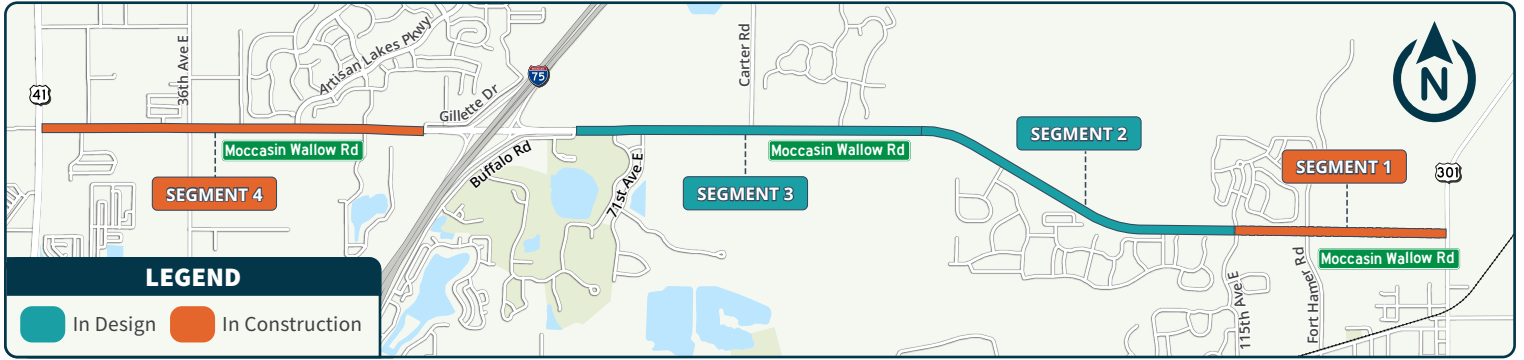

SEGMENT 1 (U.S. Highway 301 to 115th Avenue East):

ANTICIPATED COST AND CONSTRUCTION SCHEDULE

- Construction Cost:** \$28 Million
- Construction Start:** January 2023
- Completion Date:** Fall 2024

This roadway project will widen approximately one mile of Moccasin Wallow Road from two lanes to four lanes (two in each direction) between U.S. 301 and 115th Avenue East. This roadway segment will also include a 12-foot-wide multi-use path on the north side of Moccasin Wallow Road, a 6-foot-wide sidewalk on the south side, and 7-foot-wide bicycle lanes in each direction.

Median openings will be provided for access to residential communities and the addition of pedestrian-activated crossings, street lighting, signalized intersections, driveway modifications, and dedicated turn lanes will improve safety and traffic operations throughout the roadway corridor.

This segment also includes construction of a roundabout at the U.S. 301 and Moccasin Wallow Road intersection for more efficient traffic flow and improved safety. Roadway drainage will be improved and stormwater run off will be directed to new linear ponds along Moccasin Wallow Road and county right-of-way near the U.S. 301 roundabout.

Current Activities:

Sodding and the installation of curbing and sidewalks are nearing completion. Other activities include the finalization of traffic signal and streetlighting work. Travelers are reminded to exercise caution and observe the new traffic patterns and construction vehicles operating within the project area.

SEGMENT 2 (115th Avenue East to Bay Winds Parkway):

ANTICIPATED COST AND CONSTRUCTION SCHEDULE


- Construction Cost:** \$35 Million
- Construction Start:** December 2024
- Completion Date:** Mid 2026

This roadway project will widen approximately 1.6 miles of Moccasin Wallow Road from two lanes to four lanes (two in each direction) between 115th Avenue East and Bay Winds Parkway. This roadway segment will also include a 12-foot-wide multi-use path on the north side of Moccasin Wallow Road, a 6-foot-wide sidewalk on the south side, and 7-foot-wide bicycle lanes in each direction.

Median openings will be provided for access to residential communities and the addition of pedestrian-activated crossings, street lighting, signalized intersections, driveway modifications, and dedicated turn lanes will improve safety and traffic operations. Roadway drainage will be improved and stormwater run-off will be directed to new linear ponds along Moccasin Wallow Road.



Moccasin Wallow Road Improvements from U.S. 41 to U.S. 301 Bi-Weekly Update | November 20, 2024

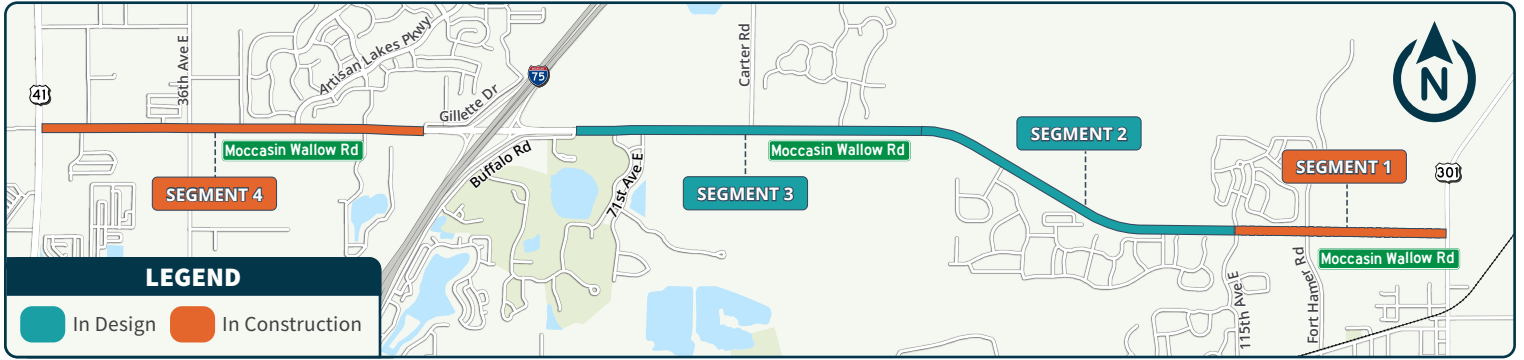

Current Activities:

Clearing activities have begun within the right-of-way along the north side of Moccasin Wallow Road. Construction is anticipated to begin in early December 2024 (weather permitting).

SEGMENT 3 (Bayside Community Church to Buffalo Road (east of I-75)):

ANTICIPATED COST AND CONSTRUCTION SCHEDULE	
	Construction Cost: \$43 Million
	Construction Start: Spring 2025
	Completion Date: Early 2027

This roadway project will widen approximately 1.8 miles of Moccasin Wallow Road from two lanes to four lanes (two in each direction) between Bayside Community Church and Buffalo Road. This roadway segment will also include a 12-foot-wide multi-use path on the north side of Moccasin Wallow Road, a 6-foot-wide sidewalk on the south side, and 7-foot-wide bicycle lanes in each direction.

Median openings will be provided for access to residential communities and the addition of pedestrian activated crossings, street lighting, signalized intersections, driveway modifications, and dedicated turn lanes will improve safety and traffic operations. Roadway drainage will be improved and stormwater run-off will be directed to new linear ponds along Moccasin Wallow Road.

Current Activities:

This project is currently in design. Land acquisition and environmental permitting are ongoing.

SEGMENT 4 (U.S. 41 to Gillette Drive):

ANTICIPATED COST AND CONSTRUCTION SCHEDULE	
	Construction Cost: \$49 Million
	Construction Start: January 2023
	Completion Date: Fall 2024


This roadway project will widen approximately 1.9 miles of Moccasin Wallow Road from two lanes to four lanes (two in each direction) between Gillette Drive (located just west of I-75) and U.S. 41. This roadway segment will also include a 12-foot-wide multi-use path on the north side of Moccasin Wallow Road, a 6-foot-wide sidewalk on the south side, and 7-foot-wide bicycle lanes in each direction.

Median openings will be provided for access to residential communities and the addition of pedestrian activated crossings, street lighting, signalized intersections, driveway modifications, and dedicated turn lanes will improve safety and traffic operations. Roadway drainage will be improved and stormwater run-off will be directed to new linear ponds along Moccasin Wallow Road.



Moccasin Wallow Road Improvements from U.S. 41 to U.S. 301


Bi-Weekly Update | November 20, 2024

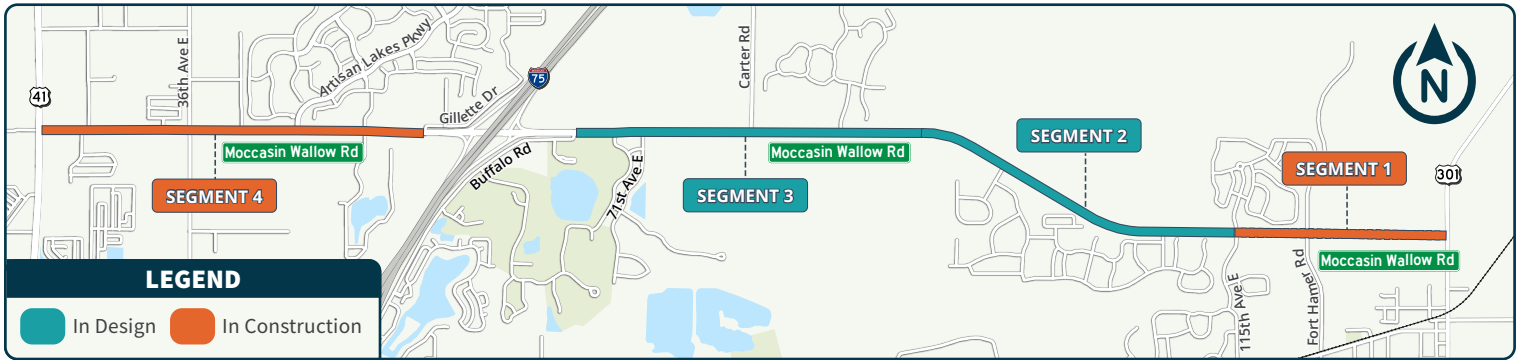



Current Activities:

Road grading, paving, and sodding continue as the contractor nears the final phase of Segment 4. Other activities include the installation of the multi-use path, sidewalk, curbing, and overhead signal tie-in. Construction on the **northern side of Moccasin Wallow Road in the western/southbound lanes of Artisan Lakes Parkway** is ongoing, with traffic shifts in place to route travelers around the work zone. Traffic on Moccasin Wallow Road and access from Artisan Lakes Parkway to Moccasin Wallow Road is being maintained. Bud Rhoden Road will remain closed at Moccasin Wallow Road through **late November 2024** to accommodate construction activities. A detour is in place to direct travelers.

CONTACT US

 **Tina Allen**
Community Outreach Specialist

 info@MoccasinWallowRoad.com

 (941) 213-1141



Project Website:
www.moccasinwallowroad.com



For more information, scan the QR code to visit the project website.
