




# Moccasin Wallow Road Improvements from U.S. 41 to U.S. 301 Bi-Weekly Update | May 5, 2025

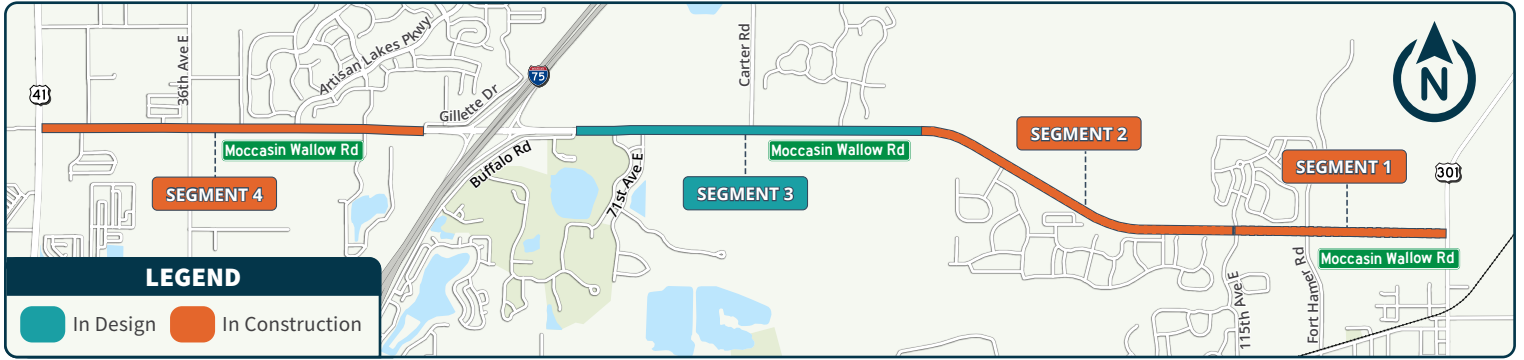

## SEGMENT 1 (U.S. Highway 301 to 115th Avenue East):

**ANTICIPATED COST AND CONSTRUCTION SCHEDULE**

- Construction Cost:** \$28 Million
- Construction Start:** January 2023
- Completion Date:** Early 2025

This roadway project widens approximately one mile of Moccasin Wallow Road from two lanes to four lanes (two in each direction) between U.S. 301 and 115th Avenue East. This roadway segment also includes a 12-foot-wide multi-use path on the north side of Moccasin Wallow Road, a 6-foot-wide sidewalk on the south side, and 7-foot-wide bicycle lanes in each direction.

Median openings are provided for access to residential communities and the addition of pedestrian-activated crossings, street lighting, signalized intersections, driveway modifications, and dedicated turn lanes improve safety and traffic operations throughout the roadway corridor.

This segment also includes a roundabout at the U.S. 301 and Moccasin Wallow Road intersection for more efficient traffic flow and improved safety. Roadway drainage has also been improved, with stormwater run off directed to new linear ponds along Moccasin Wallow Road and county right-of-way near the U.S. 301 roundabout.

### Current Activities:

The contractor is continuing with work on pavement markings, the installation of signage, and cleanup/closeout items as Segment 1 nears completion.

## SEGMENT 2 (115th Avenue East to Bay Winds Parkway):

**ANTICIPATED COST AND CONSTRUCTION SCHEDULE**


- Construction Cost:** \$35 Million
- Construction Start:** December 2024
- Completion Date:** Mid 2026

This roadway project will widen approximately 1.6 miles of Moccasin Wallow Road from two lanes to four lanes (two in each direction) between 115th Avenue East and Bay Winds Parkway. This roadway segment will also include a 12-foot-wide multi-use path on the north side of Moccasin Wallow Road, a 6-foot-wide sidewalk on the south side, and 7-foot-wide bicycle lanes in each direction.

Median openings will be provided for access to residential communities and the addition of pedestrian-activated crossings, street lighting, signalized intersections, driveway modifications, and dedicated turn lanes will improve safety and traffic operations. Roadway drainage will be improved and stormwater run-off will be directed to new linear ponds along Moccasin Wallow Road.



# Moccasin Wallow Road Improvements from U.S. 41 to U.S. 301 Bi-Weekly Update | May 5, 2025

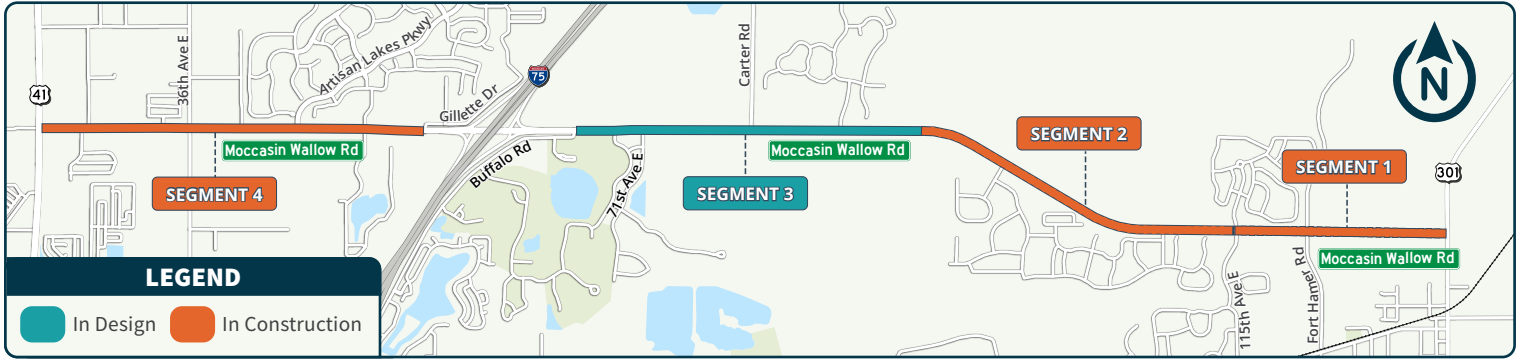

### Current Activities:

Storm drain, waterline, embankment, and private utility relocation activities are ongoing. A traffic switch is currently in effect on Moccasin Wallow Road at Summerwoods Drive to accommodate construction activities. Daily lane closures will also be in effect on Moccasin Wallow Road at Sawgrass Road Monday through Friday, between the hours of 9 a.m. and 3 p.m., as the contractor performs utility line construction activities. Travelers should expect delays as traffic is reduced to one lane to accommodate this activity.

### SEGMENT 3 (Bayside Community Church to Buffalo Road (east of I-75)):

ANTICIPATED COST AND CONSTRUCTION SCHEDULE	
	<b>Construction Cost:</b> \$43 Million
	<b>Construction Start:</b> Summer 2025
	<b>Completion Date:</b> Early 2027

This roadway project will widen approximately 1.8 miles of Moccasin Wallow Road from two lanes to four lanes (two in each direction) between Bayside Community Church and Buffalo Road. This roadway segment will also include a 12-foot-wide multi-use path on the north side of Moccasin Wallow Road, a 6-foot-wide sidewalk on the south side, and 7-foot-wide bicycle lanes in each direction.

Median openings will be provided for access to residential communities and the addition of pedestrian activated crossings, street lighting, signalized intersections, driveway modifications, and dedicated turn lanes will improve safety and traffic operations. Roadway drainage will be improved and stormwater run-off will be directed to new linear ponds along Moccasin Wallow Road.

### Current Activities:

This project is completing its land acquisition phase. The bid process is underway, with a contract award expected in June 2025.

### SEGMENT 4 (U.S. 41 to Gillette Drive):


ANTICIPATED COST AND CONSTRUCTION SCHEDULE	
	<b>Construction Cost:</b> \$49 Million
	<b>Construction Start:</b> January 2023
	<b>Completion Date:</b> April 2025

This roadway project widens approximately 1.9 miles of Moccasin Wallow Road from two lanes to four lanes (two in each direction) between Gillette Drive (located just west of I-75) and U.S. 41. This roadway segment also includes a 12-foot-wide multi-use path on the north side of Moccasin Wallow Road, a 6-foot-wide sidewalk on the south side, and 7-foot-wide bicycle lanes in each direction.



# Moccasin Wallow Road Improvements from U.S. 41 to U.S. 301

Bi-Weekly Update | May 5, 2025

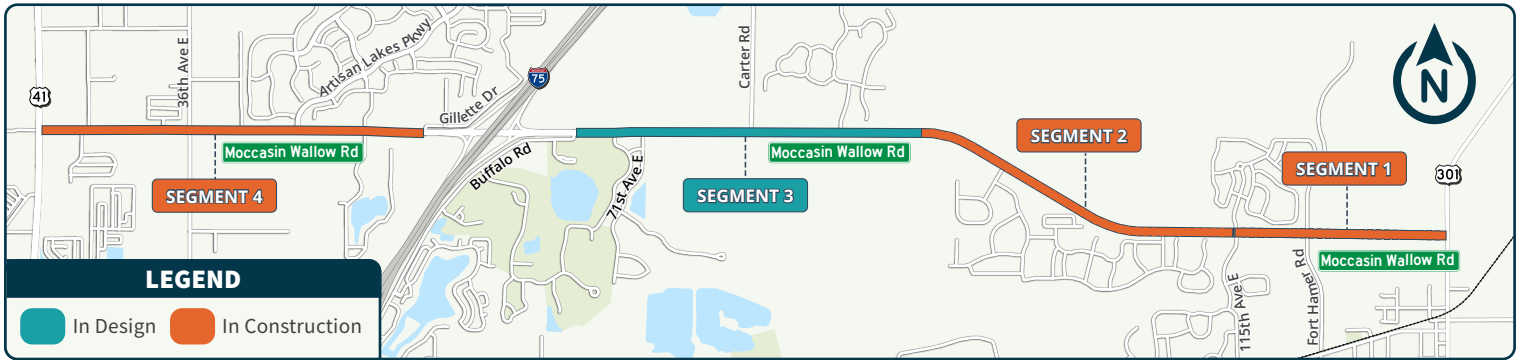

Median openings are provided for access to residential communities and the addition of pedestrian activated crossings, street lighting, signalized intersections, driveway modifications, and dedicated turn lanes improve safety and traffic operations. Roadway drainage is improved with stormwater run-off directed to new linear ponds along Moccasin Wallow Road.

### Current Activities:

The contractor is performing final activities as work on Segment 4 nears completion. Throughout the month of May 2025, construction related to the Southpointe community development will be underway on Moccasin Wallow Road, between Bud Rhoden Road and Artisan Lakes Boulevard. Mobilization of materials and equipment in preparation for the installation of a new reclaimed utility line to extend underneath I-75, from Gillette Drive to Buffalo Road, is also underway. Travelers should exercise caution and observe traffic patterns, construction crews, vehicles and equipment when traveling through the project area.

### CONTACT US

**Tina Allen**  
Community Outreach Specialist  
 [info@MoccasinWallowRoad.com](mailto:info@MoccasinWallowRoad.com)  
 (941) 213-1141

**Project Website:**  
[www.moccasinwallowroad.com](http://www.moccasinwallowroad.com)



For more information, scan the QR code to visit the project website.
